

Date	15 February 2025	Maximum Marks	5 Marks
Team ID	SWTID-2026-5019	Project Name	Import Data using Transform Maps (Spreadsheet)

PROJECT PLANNING PHASE

Project Planning Template

Scrum Methodology & Estimation

ServiceNow ETL Implementation Track

PROJECT OVERVIEW & CONTEXT

This micro project focuses on importing structured bulk employee data from an external Excel spreadsheet into ServiceNow using **Import Sets** and **Transform Maps**. It simulates a corporate onboarding scenario where spreadsheet data is loaded into a staging table (u_imp_employee_data), transformed into the live sys_user table, deduplicated via coalesce logic, and audited for complete data integrity.

Product Backlog, Sprint Schedule, and Estimation					Evaluation Weight: 4 Marks	
Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Data Ingestion & Staging	USN-1	As an administrator, I can configure an Excel Data Source (.xlsx) in ServiceNow to ingest bulk employee records.	5	High	
Sprint-1	Data Ingestion & Staging	USN-2	As an administrator, I can load spreadsheet records into a dedicated Import Set staging table (u_imp_employee_data) for data quarantine.	5	High	
Sprint-1	Data Ingestion & Staging	USN-3	As an administrator, I can preview staging table rows to verify row counts and inspect columns against source headers.	5	Medium	
Sprint-1	Data Ingestion & Staging	USN-4	As an administrator, I can configure header row indexing and date format parameters to prevent staging ingest errors.	5	High	
Sprint-2	Field Mapping & Deduplication	USN-5	As an administrator, I can create a Transform Map linking the staging table to the target User table (sys_user).	5	High	
Sprint-2	Field Mapping & Deduplication	USN-6	As an administrator, I can run 'Auto Map Matching Fields' to bind 1:1 columns (Name, Email, Phone) between staging and target schema.	5	High	
Sprint-2	Field Mapping & Deduplication	USN-7	As an administrator, I can configure choice handling for reference fields (Department, Location) to avoid orphan references.	5	Medium	
Sprint-2	Field Mapping & Deduplication	USN-8	As an administrator, I can mark user_name and email as Coalesce fields to update existing users and eliminate duplicate records.	5	High	
Sprint-3	Transform Scripts & Execution	USN-9	As a developer, I can write an onBefore script to sanitize text formatting and normalize corporate email strings.	5	High	
Sprint-3	Transform Scripts & Execution	USN-10	As an administrator, I can execute the batch transformation to commit records into the target sys_user table.	5	High	
Sprint-4	Verification & Audit Controls	USN-11	As a QA analyst, I can review the Transform History log (sys_import_set_run) to audit inserted, updated, and skipped rows.	5	High	
Sprint-4	Verification & Audit Controls	USN-12	As an HR specialist, I can cross-validate populated sys_user profiles against source spreadsheet rows to guarantee 100% data fidelity.	5	High	

Project Tracker (Planned vs. Actual Sprint Timeline)

Cadence: 6 Days per Sprint • 20 Story Points / Sprint

Sprint	Total Story Points	Duration & Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	20	6 Days • 17 Feb 2025	22 Feb 2025	20	22 Feb 2025
Sprint-2	20	6 Days • 24 Feb 2025	01 Mar 2025	20	01 Mar 2025
Sprint-3	20	6 Days • 03 Mar 2025	08 Mar 2025	20	08 Mar 2025
Sprint-4	20	6 Days • 10 Mar 2025	15 Mar 2025	20	15 Mar 2025

Velocity Formulation & Analysis

Formula Derivation

Velocity measures the volume of work a development team successfully delivers within a fixed sprint cadence. As defined in the template curriculum, for an agile team executing a sprint, the team's average velocity (AV) per iteration unit (story points per day) is derived as:

BENCHMARK EXAMPLE (TEMPLATE):

$$AV = \frac{\text{Velocity}}{\text{Sprint Duration}} = \frac{20 \text{ story points}}{10 \text{ days}} = 2 \text{ story points / day}$$

PROJECT EXECUTION VELOCITY (OUR TEAM):

$$AV = \frac{\text{Completed Story Points}}{\text{Sprint Duration (Days)}} = \frac{20 \text{ story points}}{6 \text{ days}} \approx 3.33 \text{ story points / day}$$

Sprint-1 Focus

Ingestion & Staging

Configured Excel Data Source loader, mapped header row 1, and verified data quarantine within staging table u_imp_employee_data.

Sprint-2 Focus

Mapping & Coalesce

Built Transform Map targeting sys_user. Executed Auto-Map Matching Fields and set Coalesce on User ID to eliminate duplicate profiles.

Sprint-3 Focus

Scripting & Batch Run

Developed onBefore normalization scripts for date and department resolution. Executed complete batch transform into live database.


Sprint-4 Focus

Auditing & Sign-off

Audited Transform History run logs (sys_import_set_run) verifying 100% successful inserts/updates with zero failed rows.

Burndown Chart: A burn down chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum. However, burn down charts can be applied to any project containing measurable progress over time. It compares the planned ideal trajectory against actual delivered story points across iteration days.

Sprint-1 Burndown Chart: Remaining Work (Story Points) vs. Timeline (Days)

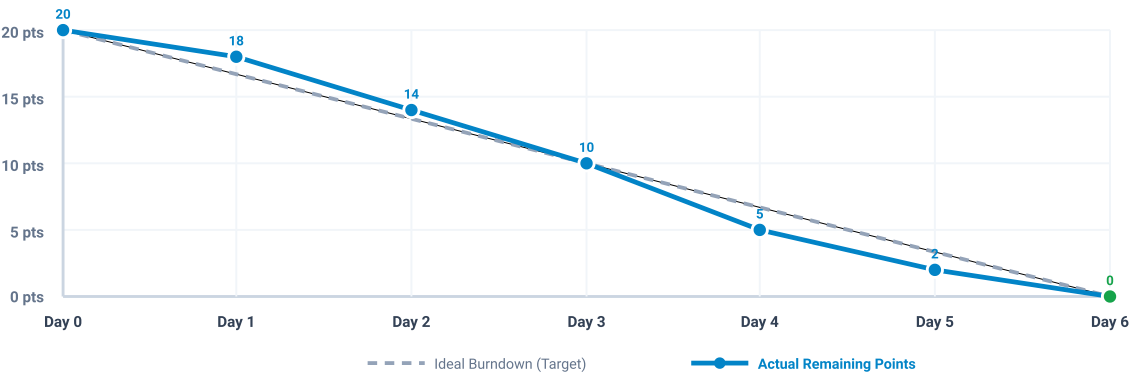

Day	Ideal Remaining	Actual Remaining	Work Delivered / Milestone Accomplished	Status
Day 0	20.0 pts	20 pts	Sprint backlog committed; user story requirements finalized for staging pipeline.	Baseline
Day 1	16.7 pts	18 pts	Configured Excel Data Source loader and indexed column headers.	In Progress
Day 2	13.3 pts	14 pts	Loaded spreadsheet records into staging table u_imp_employee_data.	In Progress
Day 3	10.0 pts	10 pts	Configured Transform Map and executed Auto-Map matching fields.	On Schedule
Day 4	6.7 pts	5 pts	Established Coalesce rules on User ID to eliminate duplicate employee records.	Ahead of Target
Day 5	3.3 pts	2 pts	Executed full batch transformation and initiated Transform History error log review.	Ahead of Target
Day 6	0.0 pts	0 pts	Validated live sys_user table; achieved 100% data parity and closed sprint.	Completed

AGILE & SCRUM REFERENCE RESOURCES

- Atlassian Project Management: atlassian.com/agile/project-management
 - Scrum with Jira Software: atlassian.com/agile/tutorials/how-to-do-scrum
 - Epics & Story Estimation: atlassian.com/agile/tutorials/epics
- Agile Burndown Charts Guide: atlassian.com/agile/tutorials/burndown-charts
 - Visual Paradigm Scrum Chart: visual-paradigm.com/scrum/scrum-burndown-chart
 - Sprints & Velocity Best Practices: atlassian.com/agile/tutorials/sprints
